

Start Jan 20, 2017

Work Order ID 154578

154578

Page 1

Thursday, December 15, 2016 11:23:13 AM

Item ID: D209-669-013 Accept *N900040100* Setup Start *NS1*
Revision ID: Stop *NS2*
Item Name: AH-1F/P/S Skidtube LH with Standard Wearplates
Start Date: 12/19/2016 Start Qty: 1.00 *1* Cust Item ID:
Required Date: 1/5/2017 Req'd Qty: 1.00 *1* Customer:
Reference:

Approvals: Process Plan: VS Date: 16/12/5 Tooling: _____ Date: _____ Run Start *NR1*
QC: _____ Date: _____ SPC (Y/N): _____ Date: _____ Stop *NR2*

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
Draw Nbr	Revision Nbr								
D209-669-013	Rev B (DEO)								
DSI 9450	Rev A								
100	Document Control								
100	DOCUMENT CONTROL								
DC	Memo								
Doc.Control -USB or Paperwork	Photocopy bluefile & type labels per PPP d209-669-013 CHG004								
110	Pick Kit								
110									
Packaging	Memo								
Packaging									

B154580

DQA: _____ Date: _____

WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval		
Description Work Order Deviation				Disposition					
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐							
		OTHER : ☐							

Work Order ID 154578

Thursday, December 15, 2016 11:23:13 AM

154578

Page 2

Item ID: D209-669-013

Accept

N900040100

Setup Start

NS1

Revision ID:

Stop

NS2

Item Name: AH-1F/P/S Skidtube LH with Standard Wearplates

Start Date: 12/19/2016 Start Qty: 1.00

1

Cust Item ID:

Required Date: 1/5/2017 Req'd Qty: 1.00

1

Customer:

Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____

Run Start

NR1

QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Stop

NR2

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
120	QC4- 100% Inspect kits for completeness	0.00							
120									
QC	Memo	0.01							
Quality Control									
130	Packaging	0.00							
130									
Packaging	Memo	0.00							
Packaging	Identify and pack for shipping as per PPPD209-669-013 Location: <u>3010</u>								
140	QC21- Final Inspection - Work Order Release	0.00							
140									
QC	Memo	0.02							
Quality Control									

JAN 24 2017

JAN 24 2017

JAN 24 2017

UMF
12-1-24

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval 		
Description Work Order Deviation				Disposition					
							Completed By		
							Lead hand / Supervisor Approval Verification		
							QC / QA Coordinator Approval		

Root Cause				FAULT CATEGORY			
Environment ☐	☐	No Re-verification ☐	☐	Pressure/Forced ☐	☐	Temperature/Cure ☐	☐
Design ☐	☐	Operator ☐	☐	Bending ☐	☐	Set-up ☐	☐
Doc/Data ☐	☐	Offset/Setup ☐	☐	Centre Not Concentric ☐	☐	BOM/Route ☐	☐
Equip/Tooling ☐	☐	Supplier ☐	☐	Cracks ☐	☐	Broken/Damage/Defect ☐	☐
Handling/Pre ☐	☐	Training ☐	☐	Crimp/Kink/Ripple/Wave ☐	☐	Inspection Incomplete/Unqualified ☐	☐
Material ☐	☐	Use for Testing ☐	☐	Cuffs ☐	☐	Contamination ☐	☐
Internal Transport ☐	☐	Poor Information ☐	☐	Crushing ☐	☐	Countersink ☐	☐
Tribal Knowledge ☐	☐	Rushing ☐	☐	Heat Treat ☐	☐	Cut Too Short ☐	☐
LOA ☐	☐	Product Improvement ☐	☐	Wave/Twist in Tube ☐	☐	Instructions Incomplete/Unclear ☐	☐
Substation ☐	☐	Process Improvement ☐	☐	Marks/Chatter ☐	☐	Drill Holes ☐	☐
Past Expiry Date ☐	☐	Manufacturing Process ☐	☐	OTHER : _____			
Misidentified ☐	☐	Past Due ☐	☐				

Picklist Print

Thursday, December 15, 2016 11:23:19 AM

Page 1

Work Order ID: 154578

154578

Parent Item: D209-669-013

D209-669-013

Parent Item Name: AH-1F/P/S Skidtube LH with Standard Wearplates

Start Date: 12/19/2016

Required Date: 1/5/2017

Start Qty: 1.00

Required Qty: 1.00

Comments: New IPP 08.02.13 LL, verified by:DD
IPP Rev:B 08-05-20 chg QTY of D2570 DD verified by: IPP REV:C
12.06.07 ECN 12-599 DD VERF:EC

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
D209-669-043		Manufactured	No			110	Each	0.0000	1	1			
D209-669-043									**	B/54580			
AH-1F/P/S Replacement Skidtube with Standard Wearplates, Fits LH or RH													
D2917-1		Manufactured	No			110	Each	0.0000	2	2			
D2917-1									**	154583			
Saddle LH													
D2918-1		Manufactured	No			110	Each	1.0000	2	2			
D2918-1									**	154584			
Saddle LH													
				<u>Location</u>		<u>Loc Qty</u>	<u>Loc Code</u>						
				ST406		1							
				141669		1							
AN4-51A		Purchased	No			110	Each	132.0000	8	8			
AN4-51A									**				
Bolt													
				<u>Location</u>		<u>Loc Qty</u>	<u>Loc Code</u>						
				FG		5							
				122993		5							
				over003		50							
				m136301		50							
				over004		24							
				m135158		24							
				ST340		53							
				m135706		3							
				m135766		50							

DAS
28
9-89

JAS
28
9-89

JAN 20 2017

DAS
6
9-89

JAN 20 2017

DAS
27
9-89

DAS
6
9-89

JAN 10 2017

DAS
27
9-89

JAS
28
9-89

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval		
Description Work Order Deviation				Disposition					
Root Cause		FAULT CATEGORY							
Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐				
Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐				
Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐				
Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐				
Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐				
Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐				
Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐				
Tribal Knowledge ☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐				
LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐				
Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐				
Past Expiry Date ☐	Manufacturing Process ☐	OTHER :							
Misidentified ☐	Past Due ☐								

Picklist Print

Thursday, December 15, 2016 11:23:19 AM

Page 2

Work Order ID: 154578

154578

Parent Item: D209-669-013

D209-669-013

Parent Item Name: AH-1F/P/S Skidtube LH with Standard Wearplates

Start Date: 12/19/2016

Required Date: 1/5/2017

Start Qty: 1.00

Required Qty: 1.00

D2570

Manufactured No

110

Each

212.0000

24

24

D2570

Bushing

**

DAS
6
9-89

DAS
28
9-89

JAN 10 2017

DAS
27
9-89

Location

Loc Qty

Loc Code

FG	12	
88781	12	
FP001	31	
147395	16	
150641	15	
ST008	169	
145728	2	
148174	25	
150641	142	

MS21042L4

Purchased No

110

Each

2,530.000

24

24

MS21042L4

Nut

**

JAN 10 2017 DAS
28
9-89

DAS
6
9-89

Location

Loc Qty

Loc Code

FP001	18	
m133363	18	
GA	192	
m135058	192	
OVER007	1500	
m136182	500	
m136295	1000	
ST303	820	
m135864	320	
m135979	500	

DAS
27
9-89

24

Thursday, December 15, 2016 11:23:19 AM

Shop Packet Print

Page 2

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date : _____		Step #: _____		QTY Effective : _____			MRB (QSI042) Approval 		
Description Work Order Deviation				Disposition					
							Completed By		
							Lead hand / Supervisor Approval Verification		
							QC / QA Coordinator Approval		

Root Cause			FAULT CATEGORY					
Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐			
Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐			
Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐			
Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐			
Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐			
Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐			
Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐			
Tribal Knowledge ☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐			
LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐			
Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐			
Past Expiry Date ☐	Manufacturing Process ☐	OTHER : _____						
Misidentified ☐	Past Due ☐							

Picklist Print

Thursday, December 15, 2016 11:23:19 AM

Work Order ID: 154578

154578

Parent Item: D209-669-013

D209-669-013

Parent Item Name: AH-1F/P/S Skidtube LH with Standard Wearplates

Start Date: 12/19/2016

Required Date: 1/5/2017

Start Qty: 1.00

Required Qty: 1.00

AN5-36A Purchased No

110 Each

126.0000

4

4

AN5-36A

Bolt

**

JAN 09 2017

DAS

6

DAS

28

9-89

Location

Loc Qty

Loc Code

over004

100

M136150

100

ST336

26

M135774

26

NAS1149D0563I Purchased No

110 Each

1,291.000

8

8

NAS1149D0563.I

Washer

**

JAN 09 2017

DAS

6

DAS

28

9-89

Location

Loc Qty

Loc Code

GA

681

m136295

681

ST263

610

m135470

3

m135774

607

MS21042L5 Purchased No

110 Each

371.0000

4

4

MS21042I 5

Nut

**

JAN 09 2017

DAS

6

DAS

28

9-89

Location

Loc Qty

Loc Code

GA

21

m127813

21

ST303

350

m135297

2

m135774

48

m136047

200

m136295

100

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date : _____		Step #: _____		QTY Effective : _____			MRB (QSI042) Approval		
Description Work Order Deviation				Disposition				Completed By	
								Lead hand / Supervisor Approval Verification	
								QC / QA Coordinator Approval	
Root Cause		FAULT CATEGORY							
Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐	No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐	Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐	Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐	Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabeled ☐ Fit/Function ☐ Misaligned/off center ☐	Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐	OTHER : _____			

Picklist Print

Thursday, December 15, 2016 11:23:19 AM

Work Order ID: 154578

154578

Parent Item: D209-669-013

D209-669-013

Parent Item Name: AH-1F/P/S Skidtube LH with Standard Wearplates

Start Date: 12/19/2016

Required Date: 1/5/2017

Start Qty: 1.00

Required Qty: 1.00

AN4-7A Purchased No

110 Each

136.0000

16

16

JAN 09 2017

AN4-7A

Bolt

**

DAS
6
9-89

DAS
28
9-89

Location

Loc Qty

Loc Code

ST345

136

m134249

3

m134754

33

m136192

100

16

DAS
27
9-89

NAS1149D0463J Purchased No

110 Each

4,058.000

32

32

JAN 09 2017

NAS1149D0463J

Washer

**

DAS
6
9-89

DAS
28
9-89

Location

Loc Qty

Loc Code

GA

80

M134508

13

M135056

67

ST260a

2200

M136192

600

M136263

600

M136406

1000

ST263

1778

M135671

3

M135948

175

M136044

1600

22

DAS
6
9-89

DAS
28
9-89

D2929 Manufactured No

110 Each

63.0000

2

2

JAN 09 2017

D2929

Spacer

**

DAS
27
9-89

Location

Loc Qty

Loc Code

Mezz

63

53564

19

84944

44

2

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date : _____		Step #: _____		QTY Effective : _____			MRB (QSI042) Approval		
Description Work Order Deviation				Disposition				Completed By	
								Lead hand / Supervisor Approval Verification	
								QC / QA Coordinator Approval	
Root Cause		FAULT CATEGORY							
Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐				
Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐				
Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐				
Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐				
Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐				
Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐				
Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐				
Tribal Knowledge ☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐				
LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐				
Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐				
Past Expiry Date ☐	Manufacturing Process ☐	OTHER : _____							
Misidentified ☐	Past Due ☐								

Picklist Print

Thursday, December 15, 2016 11:23:19 AM

Work Order ID: 154578

154578

Parent Item: D209-669-013

D209-669-013

Parent Item Name: AH-1F/P/S Skidtube LH with Standard Wearplates

Start Date: 12/19/2016

Required Date: 1/5/2017

Start Qty: 1.00

Required Qty: 1.00

D2930 Manufactured No

110 Each

14.0000

2

2

D2930

Spacer

**

DAS
27
9-89
JAN 09 2017

DAS
28
9-89

Location

Loc Qty

Loc Code

Mezz

14

53563

14

D3405-041

Manufactured No

110 Each

29.0000

1

1

D3405-041

Ground Handling Lug

**

DAS
27
9-89
JAN 09 2017

DAS
28
9-89

Location

Loc Qty

Loc Code

st529

19

147912

9

150833

10

ST546A

10

151325

10

AN4C47A

Purchased No

110 Each

52.0000

4

4

AN4C47A

Bolt

**

DAS
27
9-89
JAN 09 2017

DAS
28
9-89

Location

Loc Qty

Loc Code

FG

10

122491

10

ST341

42

m135054

2

m135586

16

m136269

24

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QS1042) Approval Completed By _____ Lead hand / Supervisor Approval Verification _____ QC / QA Coordinator Approval _____		
Description Work Order Deviation				Disposition					
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐							
		OTHER : _____							

Picklist Print

Thursday, December 15, 2016 11:23:19 AM

Work Order ID: 154578

154578

Parent Item: D209-669-013

D209-669-013

Parent Item Name: AH-1F/P/S Skidtube LH with Standard Wearplates

Start Date: 12/19/2016

Required Date: 1/5/2017

Start Qty: 1.00

Required Qty: 1.00

MS21043-4

Purchased

No

110

Each

1,392.000

5

5

MS21043-4

Nut

**

DAS 6 28
9-89 9-89

JAN 09 2017

Smb

Location

Loc Qty

Loc Code

FG

40

104603

40

GA

17

m132803

17

OVER007

900

m136192

300

m136263

300

m136406

300

ST302

435

m135600

35

m136148

400

5

D3405-043

Manufactured

No

110

Each

44.0000

1

1

D3405-043

Ground Handling Lug

**

DAS 6 28
9-89 9-89

JAN 09 2017

DAS 27
9-89

Location

Loc Qty

Loc Code

st529

24

147906

2

148665

10

152065

12

ST546A

20

150832

10

151326

10

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date : _____		Step #: _____		QTY Effective : _____			MRB (QSI042) Approval Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval		
Description Work Order Deviation				Disposition					
Root Cause		FAULT CATEGORY							
Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐				
Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐				
Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐				
Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐				
Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐				
Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐				
Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐				
Tribal Knowledge ☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐				
LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐				
Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐				
Past Expiry Date ☐	Manufacturing Process ☐	OTHER : _____							
Misidentified ☐	Past Due ☐								

Picklist Print

Thursday, December 15, 2016 11:23:20 AM

Work Order ID: 154578

154578

Parent Item: D209-669-013

D209-669-013

Parent Item Name: AH-1F/P/S Skidtube LH with Standard Wearplates

Start Date: 12/19/2016

Required Date: 1/5/2017

Start Qty: 1.00

Required Qty: 1.00

D3407-041 Manufactured No

110 Each

14.0000

1

1

D3407-041

Tow Ring

**

JAN 09 2017

DAS
6
9-89

DAS
28
9-89

Location

Loc Qty

Loc Code

st530

14

151900

10

152812

4

D3456-1

Manufactured No

110 Each

88.0000

1

1

D3456-1

Washer

**

JAN 09 2017

DAS
6
9-89

DAS
28
9-89

Location

Loc Qty

Loc Code

FG

7

25701

7

ST037

31

151938

31

ST038A

50

152842

50

D3417-5

Manufactured No

110 Each

124.0000

2

2

D3417-5

Washer

**

JAN 09 2017

DAS
6
9-89

DAS
28
9-89

Location

Loc Qty

Loc Code

ST035

84

149255

3

152860

81

ST038A

40

151493

40

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date : _____		Step #: _____		QTY Effective : _____			MRB (QSI042) Approval Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval		
Description Work Order Deviation				Disposition					
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐		OTHER : _____					

DART SERVICE INSTRUCTION

TO AMEND INSTALLATION INSTRUCTIONS IIN-D209-669 REV. B

INSTRUCTIONS:

- 1) FOR D209-669-011/-012/-013/-014 SKID TUBES @ CHANGE 003 AND SUBSEQUENT, MODIFY THE FOLLOWING:
 - a) REPLACE THE D2968-041 TOW RING WITH THE D3407-041 TOW RING ASSEMBLY.
 - b) REPLACE THE D2736-1 AND D2736-3 GHW LUGS WITH THE D3405-041 AND D3405-043 LUG ASSEMBLIES.
 - c) AMEND THE PARTS LIST IN SECTION 5.0 OF INSTALLATION INSTRUCTIONS IIN-D209-669 REV. B AS SHOWN ON PAGE 2 OF THIS DSI.

NOTE: ALL INSTALLATION FASTENERS FOR THE ABOVE CHANGES HAVE BEEN UPDATED. SEE THE AMENDED PARTS LIST ON PAGE 2 FOR DETAILS.

SHOP COPY
RETURN TO
ENGINEERING
UNCONTROLLED COPY
SUBJECT TO AMENDMENT
WITHOUT NOTICE
WORK ORDER
NO. 154578

Handwritten:
14/01/15

20160203 SH 141227

A	NEW ISSUE	AJS	09.02.24
REV.	DESCRIPTION	BY	DATE
DESIGN	AJS	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	AJS		
CHECKED		DRAWING NO.	REV. A
MFG. APPR.	N/A	DSI 9450	SHEET 1 OF 3
APPROVED		TITLE	SCALE
DE APPR.		SKIDTUBE INSTALLATIONS	NTS
DATE	09.02.24	COPYRIGHT © 2009 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :				MRB (QSI042) Approval	
Description Work Order Deviation				Disposition				Completed By	
								Lead hand / Supervisor Approval Verification	
Root Cause		FAULT CATEGORY							
Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐				
Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐				
Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐				
Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐				
Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐				
Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐				
Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐				
Tribal Knowledge ☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐				
LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐				
Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐				
Past Expiry Date ☐	Manufacturing Process ☐	OTHER :							
Misidentified ☐	Past Due ☐								

5.0 PARTS LIST

ITEM	QTY -011	QTY -012	QTY -013	QTY -014	QTY -041	QTY -043	PART NUMBER	DESCRIPTION
	X						D209-669-011	SKIDTUBE INSTALLATION, LH (AH-1W/J)
		X					D209-669-012	SKIDTUBE INSTALLATION, RH (AH-1W/J)
			X				D209-669-013	SKIDTUBE INSTALLATION, LH (AH-1P/F/S)
				X			D209-669-014	SKIDTUBE INSTALLATION, RH (AH-1P/F/S)
	1	1			X		D209-669-041	REPLACEMENT SKIDTUBE (AH-1W/J)
			1	1		X	D209-669-043	REPLACEMENT SKIDTUBE (AH-1P/F/S)

IS:

50	4	4	1	1			D3405-041	LUG ASSEMBLY
51	8	8	4	4			AN4C47A	BOLT
52	16	16	8	8			D2570	BUSHING
53	8	8	4	4			MS21043-4	NUT
54			1	1			D3405-043	LUG ASSEMBLY
60	1	1	1	1			D3407-041	TOW RING ASSEMBLY
61	1	1	1	1			D3456-1	WASHER
62	1	1	1	1			MS21043-4	NUT
63	2	2	2	2			D3417-5	WASHER

WAS:

50	4	4	1	1			D2736-1	GHW LUG
51	8	8	4	4			AN4-46A	BOLT
52	16	16	8	8			D2570	BUSHING
53	8	8	4	4			MS21042L4	NUT (OR MS21042-4)
54			1	1			D2736-3	GHW LUG
60	1	1	1	1			D2968-041	TOW RING
61	1	1	1	1			AN970-4	WASHER
62	1	1	1	1			MS21042L4	NUT (OR MS21042-4)

DESIGN	AJS	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	AJS		
CHECKED		DRAWING NO.	REV. A
MFG. APPR.	N/A	DSI 9450	SHEET 2 OF 3
APPROVED		TITLE	SCALE
DE APPR.		SKIDTUBE INSTALLATIONS	NTS
DATE	09.02.24	COPYRIGHT © 2009 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT THE WRITTEN PERMISSION FROM DART AEROSPACE LTD	

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE


QA Closed: _____ Date: _____

Work Order update only ☐


Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date : _____	Step #: _____	QTY Effective : _____		MRB (QSI042) Approval	
Description Work Order Deviation		Disposition			Completed By
					Lead hand / Supervisor Approval Verification
					QC / QA Coordinator Approval
Root Cause		FAULT CATEGORY			
Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐	Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐	Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐		OTHER : _____	

INSTALL TOW RING ASSEMBLY AS SHOWN BELOW (REFER TO SECTION F-F OF IIN-D209-669 REV. B.

IS:

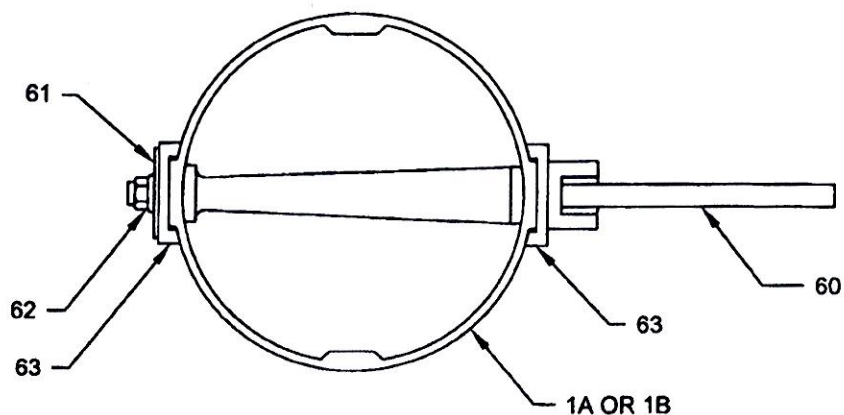

WAS:

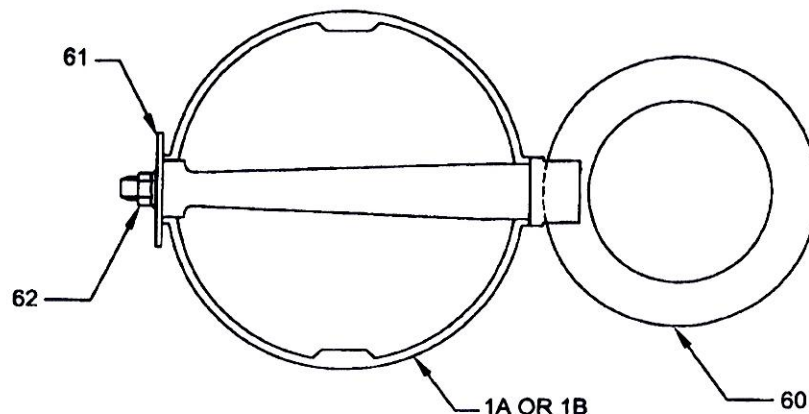

NO PICTORIAL CHANGE REQUIRED FOR GROUND HANDLING WHEEL LUG CHANGES.

DESIGN	AJS	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	AJS		
CHECKED		DRAWING NO.	REV. A
MFG. APPR.	N/A	DSI 9450	SHEET 3 OF 3
APPROVED		TITLE	SCALE
DE APPR.		SKIDTUBE INSTALLATIONS	NTS
DATE	09.02.24	COPYRIGHT © 2009 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE, IN COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD	

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date :	Step #:	QTY Effective :		MRB (QSI042) Approval	
Description Work Order Deviation		Disposition		Completed By	
				Lead hand / Supervisor Approval Verification	
				QC / QA Coordinator Approval	
Root Cause		FAULT CATEGORY			
Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐	No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐	Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐	Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐	Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabeled ☐ Fit/Function ☐ Misaligned/off center ☐	Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐
OTHER : _____					

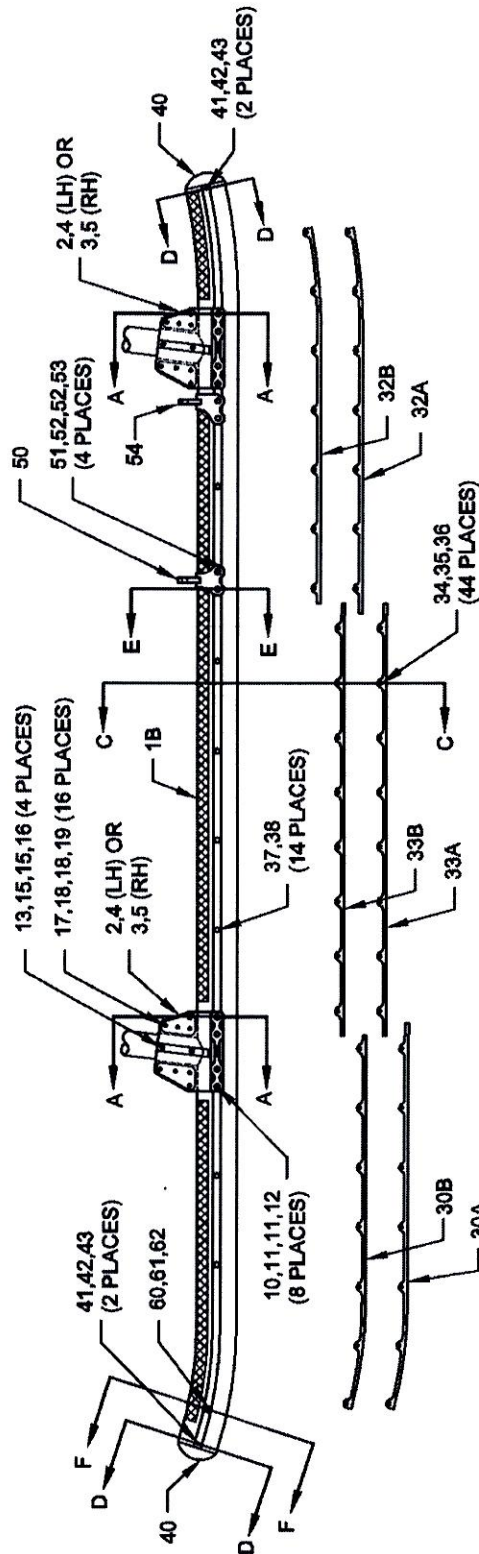


Figure 3 – D209-669-013/-014 Skidtube Installation (AH-1F/P/S)

• COPYRIGHT © 2004 BY DART AEROSPACE LTD •

THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.

Revision: **B**
Date: 07.08.23

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐							
Date :		Step #:		QTY Effective :				MRB (QSI042) Approval			
Description Work Order Deviation				Disposition				Completed By			
								Lead hand / Supervisor Approval Verification			
								QC / QA Coordinator Approval			
Root Cause				FAULT CATEGORY							
Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐		No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐		Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐		Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabeled ☐ Fit/Function ☐ Misaligned/off center ☐		Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐	
				OTHER :							

4.0 WEIGHT AND BALANCE

The following weight and balance information is for the replacement Dart parts. The weight and balance of the skidtubes that are being removed from the aircraft is the responsibility of the installer.

Installation	Weight	LONGITUDINAL	
		Arm	Moment
D209-669-011/-012	49.6 lb	170.4 in	8452 in lb
SKIDTUBE INSTALLATION	22.5 kg	4.33 m	97.4 m kg
D209-669-013/-014	43.8 lb	176.5 in	7731 in lb
SKIDTUBE INSTALLATION	19.9 kg	4.48 m	89.2 m kg

5.0 PARTS LIST

Item	Qty -011	Qty -012	Qty -013	Qty -014	Qty -041	Qty -043	Part Number	Description
	X						D209-669-011	SKIDTUBE INSTALLATION, LH (AH-1W/J)
		X					D209-669-012	SKIDTUBE INSTALLATION, RH (AH-1W/J)
			X				D209-669-013	SKIDTUBE INSTALLATION, LH (AH-1P/F/S)
				X			D209-669-014	SKIDTUBE INSTALLATION, RH (AH-1P/F/S)
	1	1			X		D209-669-041	REPLACEMENT SKIDTUBE (AH-1W/J)
			1	1		X	D209-669-043	REPLACEMENT SKIDTUBE (AH-1P/F/S)
1A					1		D2906-041	SKIDTUBE ASSEMBLY
1B						1	D2906-043	SKIDTUBE ASSEMBLY
2	1		2				D2917-1	OUTER SADDLE (FWD, LH)
3		1		2			D2917-2	OUTER SADDLE (FWD, RH)
4	1		2				D2918-1	INNER SADDLE (FWD, LH)
5		1		2			D2918-2	INNER SADDLE (FWD, RH)
6	1						D2919-1	OUTER SADDLE (AFT, LH)
7		1					D2919-2	OUTER SADDLE (AFT, RH)
8	1						D2920-1	INNER SADDLE (AFT, LH)
9		1					D2920-2	INNER SADDLE (AFT, RH)
10	8	8	8	8			AN4-51A	BOLT
11	16	16	16	16			D2570	BUSHINGS
12	8	8	8	8			MS21042L4	NUT (OR MS21042-4)
13	2	2	4	4			AN5-36A	BOLT
14	2	2					AN5-41A	BOLT
15	8	8	8	8			AN960JD516	WASHER
16	4	4	4	4			MS21042L5	NUT (OR MS21042-5)
17	16	16	16	16			AN4-7A	BOLT
18	32	32	32	32			AN960JD416	WASHER
19	16	16	16	16			MS21042L4	NUT (OR MS21042-4)

CONTINUED ON NEXT PAGE

• COPYRIGHT © 2004 BY DART AEROSPACE LTD. •

THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.

Revision: **B**
Date: 07.08.23

CONTINUED FROM PREVIOUS PAGE

20	2	2	2	2			D2929	SPACER
21	2	2	2	2			D2930	SPACER
*30A					1	1	D3564-9	WEARSHOE (REPLACES D2577-1)
*30B					1	1	D3566-1	GASKET
*31A					1		D3564-15	WEARSHOE (REPLACES 18" D2577-5)
*31B					1		D3566-15	GASKET
*32A					1	1	D3564-11	WEARSHOE (REPLACES D2577-3)
*32B					1	1	D3566-1	GASKET
*33A					1	1	D3564-5	WEARSHOE (REPLACES D2577-5)
*33B					1	1	D3566-5	GASKET
*34					50	44	AN3C4A	BOLT (REPLACES AN3-4A)
*35					50	44	AN960C10L	WASHER (REPLACES AN960JD10L)
*36					50	44	AKS7-1032-130	INSERT (OR ALS7-1032-130, OR ALS4-1032-130, OR AKS4-1032-130)
*37					12	14	D2594-1	PLUG
*38					12	14	D2594-3	O-RING
*40					2	2	D2855	AFT CAP
*41					4	4	AN3-5A	BOLT
*42					4	4	AN960JD10L	WASHER
*43					4	4	AKS7-1032-225	INSERT (OR ALS7-1032-225, OR ALS4-1032-225, OR AKS4-1032-225)
50	4	4	1	1			D2736-1	GHW LUG
51	8	8	4	4			AN4-46A	BOLT
52	16	16	8	8			D2570	BUSHING
53	8	8	4	4			MS21042L4	NUT (OR MS21042-4)
54			1	1			D2736-3	LUG ASSEMBLY
60	1	1	1	1			D2968-041	TOW RING
61	1	1	1	1			AN970-4	WASHER
62	1	1	1	1			MS21042L4	NUT (OR MS21042-4)

* DENOTES THAT PART IS INCLUDED WITH D2906-041/-043 SKIDTUBE ASSEMBLY

• COPYRIGHT © 2004 BY DART AEROSPACE LTD •

THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.

Revision: B
Date: 07.08.23

REFERENCE ONLY

5.0 PARTS LIST

ITEM	QTY -011	QTY -012	QTY -013	QTY -014	QTY -041	QTY -043	PART NUMBER	DESCRIPTION
	X						D209-669-011	SKIDTUBE INSTALLATION, LH (AH-1W/J)
		X					D209-669-012	SKIDTUBE INSTALLATION, RH (AH-1W/J)
			X				D209-669-013	SKIDTUBE INSTALLATION, LH (AH-1P/F/S)
				X			D209-669-014	SKIDTUBE INSTALLATION, RH (AH-1P/F/S)
	1	1			X		D209-669-041	REPLACEMENT SKIDTUBE (AH-1W/J)
			1	1		X	D209-669-043	REPLACEMENT SKIDTUBE (AH-1P/F/S)

IS:

50	4	4	1	1			D3405-041	LUG ASSEMBLY
51	8	8	4	4			AN4C47A	BOLT
52	16	16	8	8			D2570	BUSHING
53	8	8	4	4			MS21043-4	NUT
54			1	1			D3405-043	LUG ASSEMBLY
60	1	1	1	1			D3407-041	TOW RING ASSEMBLY
61	1	1	1	1			D3456-1	WASHER
62	1	1	1	1			MS21043-4	NUT
63	2	2	2	2			D3417-5	WASHER

WAS:

50	4	4	1	1			D2736-1	GHW LUG
51	8	8	4	4			AN4-46A	BOLT
52	16	16	8	8			D2570	BUSHING
53	8	8	4	4			MS21042L4	NUT (OR MS21042-4)
54			1	1			D2736-3	GHW LUG
60	1	1	1	1			D2968-041	TOW RING
61	1	1	1	1			AN970-4	WASHER
62	1	1	1	1			MS21042L4	NUT (OR MS21042-4)

DESIGN	AJS	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA DRAWING NO. REV. A DSI 9450 SHEET 2 OF 3 TITLE SCALE SKIDTUBE INSTALLATIONS NTS COPYRIGHT © 2009 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT THE EXPRESS WRITTEN PERMISSION OF DART AEROSPACE LTD.
DRAWN	AJS	
CHECKED		
MFG. APPR.	N/A	
APPROVED		
DE APPR.		
DATE	09.02.24	
